Architect4Hire

STATUS REPORT 01 · BASELINE · NOVEMBER 6, 2026

Project Rogers Edge

Status report for 6311arts.com

Client Sponsor: **Holly King** Architect: **Robert Felkins**

MILESTONES AT A GLANCE

Architect4Hire

Where each milestone stands

Status as of October 30, 2026 · 44 items across five milestones

1

Milestone 1 · Nov 2 – Nov 15 — Foundation & vision

*Not started · **9** of 13 items done*

2

Milestone 2 · Nov 16 – Nov 29 — Core content & platform

Not started · 0 of 14 items done

3

Milestone 3 · Nov 30 – Dec 13 — Shop, members & artists

Not started · 0 of 10 items done

4

Milestone 4 · Dec 14 – Dec 27 — Hardening & first UAT

Not started · 0 of 5 items done

5

Milestone 5 · Dec 28 – Jan 11 — UAT & launch readiness

Not started · 0 of 3 items done

HOW TO READ THIS REPORT

Status key

ON TRACK

On track

- Work started and on course for the due date
- Not started (gray) means not yet begun
- Items are due at the end of their milestone

AT RISK

At risk

- Could slip without action this period
- Say why in the This period column
- Raised in Risks and blockers on the summary

BLOCKED

Blocked

- Waiting on a decision, access or content
- Name who it's waiting on
- Raised in Decisions needed on the summary

DONE

Done

- Meets its Done when criterion
- Shown on Dev or Production, or delivered
- Counted in the milestone's done total

MILESTONE 1 · NOV 2 – NOV 16 · 7 OF 13 DONE · IN PROGRESS

Architect4Hire

Milestone 1: Foundation & vision

#	ITEM	OWNER	STATUS	DUE	DONE WHEN	THIS PERIOD
1.1	Site Audit Deck	Robert	**Done**	Nov 16	Reviewed with Holly and Michael	—
1.2	Vision Deck	Robert	**Done**	Nov 16	Direction signed off	—
1.3	Configuration of Slack	Robert	**Done**	Nov 16	Channels live; client has guest access	—
1.4	Configuration of GitHub – security and collaboration	Robert	**Done**	Nov 16	Private Read Only – Director Invited	—
1.5	Configuration of 6311arts Knowledge Base GitHub repo pages	Robert	**Done**	Nov 16	Site live; first pages published	—
1.6	Configuration of Hot Folder in OneDrive	Robert	**Done**	Nov 16	Folder shared; client uploading assets	—
1.7	Architecture and Design Document	Robert	**Done**	Nov 16	Reviewed with sponsor	—
1.8	Angular SSR Feedback Implemented	Robert	**On Track**	Nov 16	Feedback issues closed on Dev	—
1.9	Studio Feedback Implemented	Robert	**On Track**	Nov 16	Feedback issues closed on Dev	—
1.10	Azure CI/CD Implemented for Dev	Robert	**On Track**	Nov 16	Merge to main deploys Dev	—
1.11	Email Platform selection for Holly/Michael Review	Robert + Michael & Holly	**Done**	Nov 16	Platform chosen by Holly and Michael	—
1.12	Review Image Utilization	Robert + Michael	**At Risk**	Nov 16	Per-page image plan agreed	—
1.13	Google Analytics Account Set Up	Robert	**Done**	Nov 16	GA4 Dashboard is visible	—

MILESTONE 2 · NOV 16 – NOV 29 · 0 OF 14 DONE · NOT STARTED

Architect4Hire

Milestone 2: Core content & platform

#	ITEM	OWNER	STATUS	DUE	DONE WHEN	THIS PERIOD
2.1	Classes – Studio and SSR and Documentation	Robert	**Not started**	Nov 30	Staff publish a class unaided	—
2.2	Events – Studio and SSR and Documentation	Robert	**Not started**	Nov 30	Event pages live on Dev	—
2.3	Exhibitions – Studio and SSR and Documentation	Robert	**Not started**	Nov 30	Show pages live on Dev	—
2.4	Artists – Studio and SSR and Documentation	Robert	**Not started**	Nov 30	Artist pages live on Dev	—
2.5	Instructors – Studio and SSR and Documentation	Robert	**Not started**	Nov 30	Instructor pages live on Dev	—
2.6	Media – Studio and SSR and Documentation	Robert	**Not started**	Nov 30	Upload, crop, alt text working	—
2.7	Artist Login and Portal	Robert	**Not started**	Nov 30	Invited artist signs in and edits profile	—
2.8	Azure CI/CD Implemented for Production	Robert	**Not started**	Nov 30	Approved deploy reaches Production	—
2.9	Square Phase 1	Robert	**Not started**	Nov 30	Sandbox class purchase settles	—
2.10	WordPress Import	Robert	**Not started**	Nov 30	Record counts reconcile	—
2.11	Mail Provider API integration	Robert	**Not started**	Nov 30	Sign-up appears in the platform	—
2.12	SEO Field Extensions and Identification	Robert	**Not started**	Nov 30	SEO fields on every content type	—
2.13	Implement Image Improvement per Page	Robert	**Not started**	Nov 30	Image plan applied to every page	—
2.14	Google Analytics Service and Implementation	Robert	**Started**	Nov 30	Key events visible in GA4	—

MILESTONE 3 · NOV 30 – DEC 14 · 0 OF 10 DONE · NOT STARTED

Architect4Hire

Milestone 3: Shop, members & artists

#	ITEM	OWNER	STATUS	DUE	DONE WHEN	THIS PERIOD
3.1	Shop Gallery – SSR	Robert	**Not started**	Dec 14	Filter by artist, medium, price	—
3.2	Shop Details – SSR	Robert	**Not started**	Dec 14	Item page hands off to Square	—
3.3	Shop Items – Studio and Documentation	Robert	**Not started**	Dec 14	Staff add an item unaided	—
3.4	Membership	Robert	**Not started**	Dec 14	Sandbox membership purchase settles	—
3.5	SEO Implementation Phase 1	Robert	**Not started**	Dec 14	Schema, sitemap, audit fixes live	—
3.6	Page – Studio and SSR	Robert	**Not started**	Dec 14	Staff build a page in Studio	—
3.7	Artist Submission of Work	Robert	**Not started**	Dec 14	Submission reaches staff inbox	—
3.8	Artist Gallery with Live Edits	Robert	**Not started**	Dec 14	Portal edit shows on gallery	—
3.9	Featured Artist	Robert	**Not started**	Dec 14	Feature shows on Home and Artists	—
3.10	Square Phase 2	Robert	**Not started**	Dec 14	Artwork sale marks item sold	—

MILESTONE 4 · DEC 14 – DEC 28 · 0 OF 5 DONE · NOT STARTED

Milestone 4: Hardening & first User Acceptance Testing (UAT)

#	ITEM	OWNER	STATUS	DUE	DONE WHEN	THIS PERIOD
4.1	Square Integration Documentation	Robert	**Not started**	Dec 28	Staff guide and runbook published	—
4.2	Square and Mail Poet export and future path	Robert	**Not started**	Dec 28	Exports delivered; path approved	—
4.3	Redirect	Robert	**Not started**	Dec 28	Every legacy URL 301s correctly	—
4.4	SEO Implementation 2	Robert	**Not started**	Dec 28	Search Console set up; vitals checked	—
4.5	First Round of UAT	Holly, Michael	**Not started**	Dec 28	All issues logged and triaged	—

MILESTONE 5 · DEC 28 – JAN 11 · 0 OF 3 DONE · NOT STARTED

Architect4Hire


Milestone 5: UAT & launch readiness

#	ITEM	OWNER	STATUS	DUE	DONE WHEN	THIS PERIOD
5.1	First round of UAT issues resolved	Robert	**Not started**	Jan 11	Zero open launch blockers	—
5.2	Implementation of Mail Poet and Square Contacts Future Path	Robert	**Not started**	Jan 11	Contacts imported; counts reconcile	—
5.3	Second round of UAT	Holly, Michael	**Not started**	Jan 11	Sign-off from Holly and Michael	—

LET'S TALK

Questions?

Push on the ideas, the trade-offs and the order of the work — that's what this conversation is for.

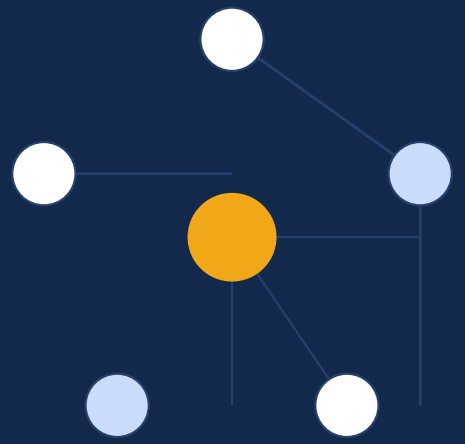

robert@architect4hire.com

(312) 493-9696

architect4hire.com
