Architect4Hire

MILESTONE PLAN · NOV 2, 2026 – JAN 11, 2027

Project Rogers Edge

Prepared for 6311Arts.com

Client Sponsor: **Holly King** Architect: **Robert Felkins**

MILESTONES

Architect4Hire

Five milestones, ten weeks

Two-week milestones, from discovery to the second round of UAT

1

Milestone 1 · Nov 2 – Nov 15 — Foundation & vision

Discovery and vision decks, team tools, architecture, Dev pipeline and the email platform pick.

2

Milestone 2 · Nov 16 – Nov 29 — Core content & platform

Six content types in Studio and on the site, artist portal, Production pipeline, Square phase 1, WordPress import.

3

Milestone 3 · Nov 30 – Dec 13 — Shop, members & artists

Shop gallery and details, membership, pages, artist submissions and galleries, Square phase 2, SEO phase 1.

4

Milestone 4 · Dec 14 – Dec 27 — Hardening & first UAT

Square documentation, MailPoet and order exports, redirects, SEO phase 2, first round of UAT.

5

Milestone 5 · Dec 28 – Jan 11 — UAT & launch readiness

First-round UAT fixes, contacts moved to their new home, second round of UAT.

Architect4Hire

MILESTONE 1 OF 5

Foundation & vision

Milestone 1 · Nov 2 – Nov 16

Agree on where we're going, stand up the team's tools, and get code deploying to Dev.

MILESTONE 1 · NOV 2 – NOV 15 · 01 OF 03

Architect4Hire

Setting direction

DISCOVERY

Discovery Deck

- Inventory of pages, ~25 plugins, content and media
- WooCommerce, FooEvents and MailPoet data mapped
- Audit findings and staff pain points reviewed

VISION

Vision Deck

- Target experience for staff, visitors, members and artists
- Angular SSR, Studio, Square, email and Azure in one picture
- Direction signed off by Holly

ARCHITECTURE

Architecture & Design Document

- Components, data model and integration seams
- Security, hosting, environments and running cost
- Decision log kept in the Knowledge Base

DECISION

Email platform selection

- Kit (the SOW baseline) compared with 1–2 alternatives
- Nonprofit pricing, list size, automation, API, ease of use
- Recommendation for Holly and Michael to approve

MILESTONE 1 · NOV 2 – NOV 15 · 02 OF 03

Architect4Hire

Team, tools & knowledge

COLLABORATION

Slack

- Channels for the project, client reviews and build alerts
- Guest access for Holly, Michael and staff
- GitHub and Azure notifications piped in

SECURITY

GitHub — security & collaboration

- 6311-owned organization, teams and roles; 2FA required
- Protected main branch with required reviews
- Secret scanning, Dependabot and a project board

KNOWLEDGE

6311arts Knowledge Base

- GitHub Pages site built from a docs repo
- Architecture, runbooks and staff how-to guides
- Publishes automatically on every merge

SHARING

OneDrive knowledge sharing folder

- One place for logos, photos, copy and artist bios
- Decks, review notes and sign-offs filed by milestone
- Permissions set for 6311 and the project team

MILESTONE 1 · NOV 2 – NOV 15 · 03 OF 03

Architect4Hire

Build foundation

FRONT END

Angular SSR feedback implemented

- Review notes on the prototype logged as GitHub issues
- Design, navigation, copy and mobile fixes applied
- Changes on Dev for a second look

STUDIO

Studio feedback implemented

- Feedback on Studio screens and workflows applied
- Labels use the words 6311 staff already use
- Changes on Dev for a second look

DEVOPS

Azure CI/CD for Dev

- GitHub Actions builds and tests every pull request
- Merge to main deploys the site and Studio to Dev
- Secrets kept in Azure, never in the repo

MEDIA

Review image utilization

- Every page's images checked: size, format, alt text
- Rights confirmed for artwork shown online
- Per-page image plan carried into Milestone 2

Architect4Hire

MILESTONE 2 OF 5

Core content & platform

Milestone 2 · Nov 16 – Nov 29

Every core content type editable in Studio and live on the site, with Production, Square and analytics in place.

ARCHITECT4HIRE.COM

MILESTONE 2 · NOV 16 – NOV 29 · 01 OF 03

Architect4Hire

Six content types, end to end

CONTENT TYPES

Classes & Events

- Classes: sessions, level, instructor, price, seat limits
- Events: openings, talks and one-off workshops
- Calendar, list and detail pages with event markup

CONTENT TYPES

Exhibitions & Artists

- Exhibitions: dates, artists, works and reception
- Artists: bio, statement, medium, portrait and links
- Current, upcoming and archive pages for shows

CONTENT TYPES

Instructors & Media

- Instructors: bio, photo and the classes they teach
- Media library: upload, crop, alt text, reuse anywhere
- Image renditions sized for every screen

DONE MEANS

Studio, SSR and documentation

- Studio: create, edit, preview, schedule, publish
- SSR: fast list and detail pages, ready for search
- Docs: a staff how-to page in the Knowledge Base

MILESTONE 2 · NOV 16 – NOV 29 · 02 OF 03

Architect4Hire

Artists, payments & email

ARTISTS

Artist login & portal

- Secure sign-in for artists invited by staff
- Artists keep their bio, portrait and links current
- Staff stay in control of what gets published

PAYMENTS

Square phase 1

- 6311's Square account connected, sandbox first
- Classes and events synced as Square items
- Square-hosted checkout for class seats

MIGRATION

WordPress import

- Pages, classes, exhibitions, artists and images
- Repeatable script, safe to rerun before launch
- Record counts reconcile with the old site

EMAIL

Mail provider API integration

- Newsletter sign-up wired to the chosen platform
- Tags for students, members and artists
- Consent and source recorded on every sign-up

MILESTONE 2 · NOV 16 – NOV 29 · 03 OF 03

Architect4Hire

Production, search & insight

DEVOPS

Azure CI/CD for Production

- Production environment with an approval gate
- Zero-downtime deploys and quick rollback
- Backups, uptime monitoring and SSL ready

SEO

SEO field extensions & identification

- Title, description, social image, canonical in Studio
- Fields on every content type, with sensible defaults
- Target keywords mapped to pages

MEDIA

Image improvement per page

- Milestone 1 image plan applied page by page
- Modern formats, responsive sizes, lazy loading
- Alt text on every image

ANALYTICS

Google Analytics

- GA4 property in 6311's own Google account
- Angular analytics service that is safe under SSR
- Key events tracked; Meta pixel carried over

Architect4Hire

MILESTONE 3 OF 5

Shop, members & artists

Milestone 3 · Nov 30 – Dec 13

Sell art and memberships through Square, give artists their own space, and make the first SEO pass.

MILESTONE 3 · NOV 30 – DEC 13 · 01 OF 03

Architect4Hire

The shop

SSR

Shop gallery

- Browse original work and merchandise
- Filter by artist, medium and price
- Sold pieces marked automatically

SSR

Shop details

- Large images, artist, medium, size and price
- Buy button hands off to Square checkout
- Product markup for rich Google results

STUDIO

Shop items — Studio & documentation

- Staff add and edit items and consignment details
- Square owns price and stock; Studio shows sync status
- Staff how-to in the Knowledge Base

PAYMENTS

Square phase 2

- Artwork, merchandise and memberships through Square
- Webhooks update sold status, seats and members
- Reconciler catches anything missed; refunds tested

MILESTONE 3 · NOV 30 – DEC 13 · 02 OF 03

Architect4Hire

Members, pages & search

MEMBERS

Membership

- Tiers and benefits page; join online
- Renewals through Square subscriptions
- Member discount and a member list for staff

CONTENT

Pages

- About, Visit, Privacy, Terms and more, built in Studio
- Flexible sections staff can arrange themselves
- Hours and address kept once, used everywhere

SEO

SEO implementation phase 1

- Structured data for events, classes, products, 6311
- XML sitemap, robots and canonical URLs
- 2026 audit fixes: hidden About page, meta descriptions

ARTISTS

Featured artist

- Staff pick the featured artist in Studio
- Shown on the Home and Artists pages
- Next feature scheduled ahead of time

MILESTONE 3 · NOV 30 – DEC 13 · 03 OF 03

Architect4Hire

Artists' own space

SUBMISSION OF WORK

- ✓ *Artists upload new work from the portal: images, medium, size, price*
- ✓ *Submissions land in a staff review inbox: new, reviewed, accepted, declined*
- ✓ *Accepted work flows into the artist's gallery and, if for sale, the shop*

GALLERY WITH LIVE EDITS

- ★ *Each artist gets a public gallery page worth sharing*
- ★ *Portal edits show in a live preview as the artist types*
- ★ *Instant or staff-approved publishing, as 6311 prefers*

Builds on the artist login and portal from Milestone 2.

Architect4Hire

MILESTONE 4 OF 5

Hardening & first UAT

Milestone 4 · Dec 14 – Dec 27

Document payments, plan the move off MailPoet and WooCommerce, protect search rankings, and put the site in front of testers.

MILESTONE 4 · DEC 14 – DEC 27 · 01 OF 02

Architect4Hire

Ready for testing

PAYMENTS

Square integration documentation

- How checkout, webhooks and sync fit together
- Staff guide: orders, class rosters and refunds
- Runbook for when something fails

DATA

Square & MailPoet export, future path

- WooCommerce order history exported to CSV
- MailPoet subscribers exported with consent data
- Plan for contacts in Square and the email platform

SEARCH

Redirects

- Every legacy WordPress URL mapped to its new page
- Permanent (301) redirects tested in bulk
- 404 monitoring to catch anything missed

SEO

SEO implementation phase 2

- Core Web Vitals tuned on key pages
- Search Console set up; sitemap submitted
- Social cards, internal links, remaining audit items

MILESTONE 4 · DEC 14 – DEC 27 · 02 OF 02

Architect4Hire

First round of UAT

WHAT WE TEST

- ✓ *Staff publish a class, show, artist and shop item unaided*
- ✓ *Test purchases of a class, an artwork and a membership*
- ✓ *Forms, sign-ups, redirects and pages on phone and desktop*

HOW IT RUNS

- ★ *Holly, Michael and staff follow short test scripts on staging*
- ★ *Issues logged in GitHub, triaged daily, fixed by priority*
- ★ *Tester availability over the holidays confirmed early*

Exit: every UAT issue logged, triaged and assigned.

Architect4Hire

MILESTONE 5 OF 5

UAT & launch readiness

Milestone 5 · Dec 28 – Jan 11

Close out the first round of findings, move contacts to their new home, and confirm the site is ready to launch.

MILESTONE 5 · DEC 28 – JAN 11 · 01 OF 01

Closing out

FIXES

First-round UAT issues resolved

- Every issue fixed, retested or deferred by agreement
- Fixes deployed to staging for retest
- Launch blocker list down to zero

CONTACTS

MailPoet & Square contacts

- Subscribers imported into the chosen email platform
- Customers and members in the Square directory
- Counts reconcile; consent carried across

UAT

Second round of UAT

- Full retest of the round-one scripts
- Sign-off from Holly and Michael
- Go / no-go decision for launch

NEXT · PER SOW

Launch & handoff

- DNS cutover and production checkout verified
- Staff training session and admin guide
- 30 days of post-launch support

WORKING TOGETHER

What we need from 6311

REVIEWS

Reviews & approvals

- One decision-maker for approvals
- Feedback within 3 business days
- Vision and email platform signed off in Milestone 1

CONTENT

Content & assets

- Logos, photos, page copy and artist bios
- Rights to publish every artwork image
- Dropped in the shared OneDrive folder

ACCESS

Accounts & access

- Square, Azure, GitHub, Google and email accounts
- Owned by 6311, with admin access for the team
- WordPress.com admin during migration

TESTING


Testing time

- Testers named for both UAT rounds
- Holiday availability confirmed
- Staff time for training before launch

LET'S TALK

Questions?

Push on the ideas, the trade-offs and the order of the work — that's what this conversation is for.

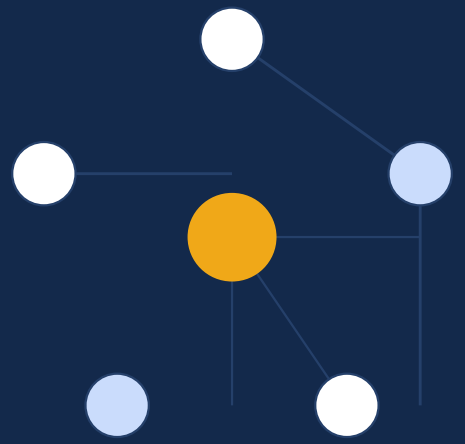

robert@architect4hire.com

(312) 493-9696

architect4hire.com
